
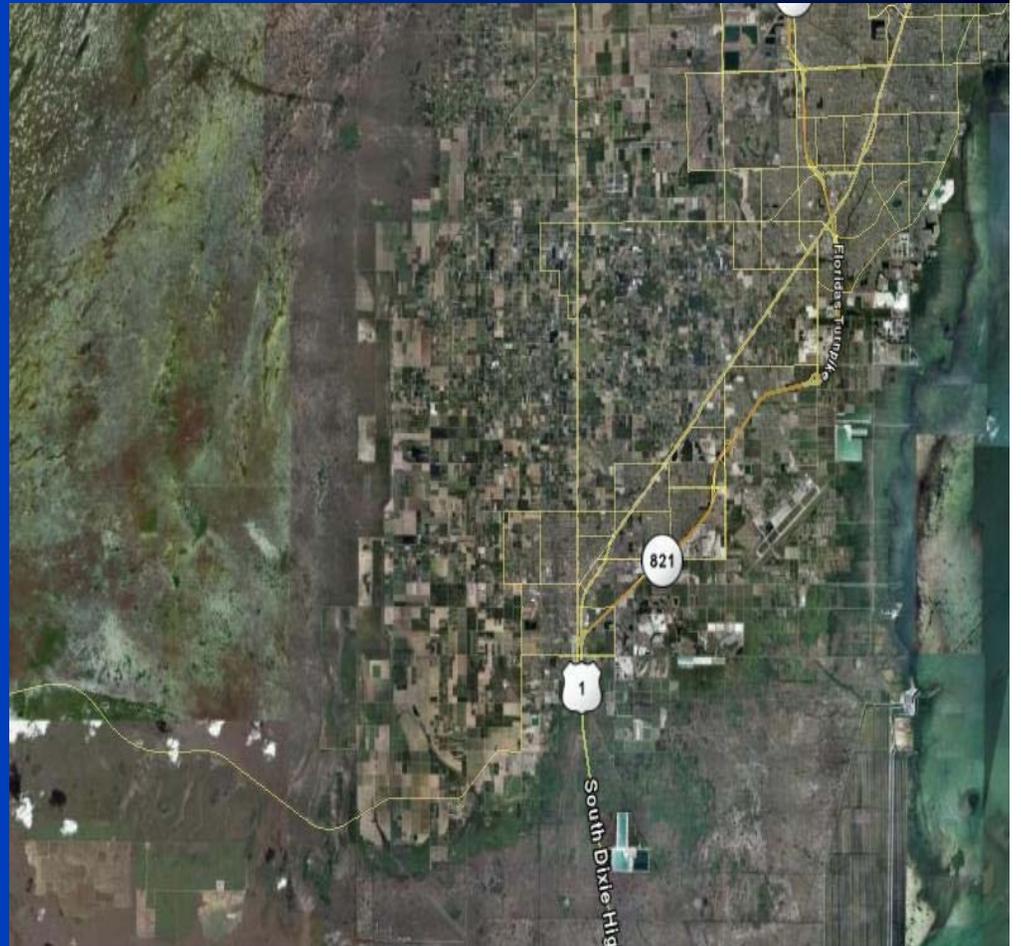


C-111 South Dade Project


TASK FORCE MEETING

December 2007

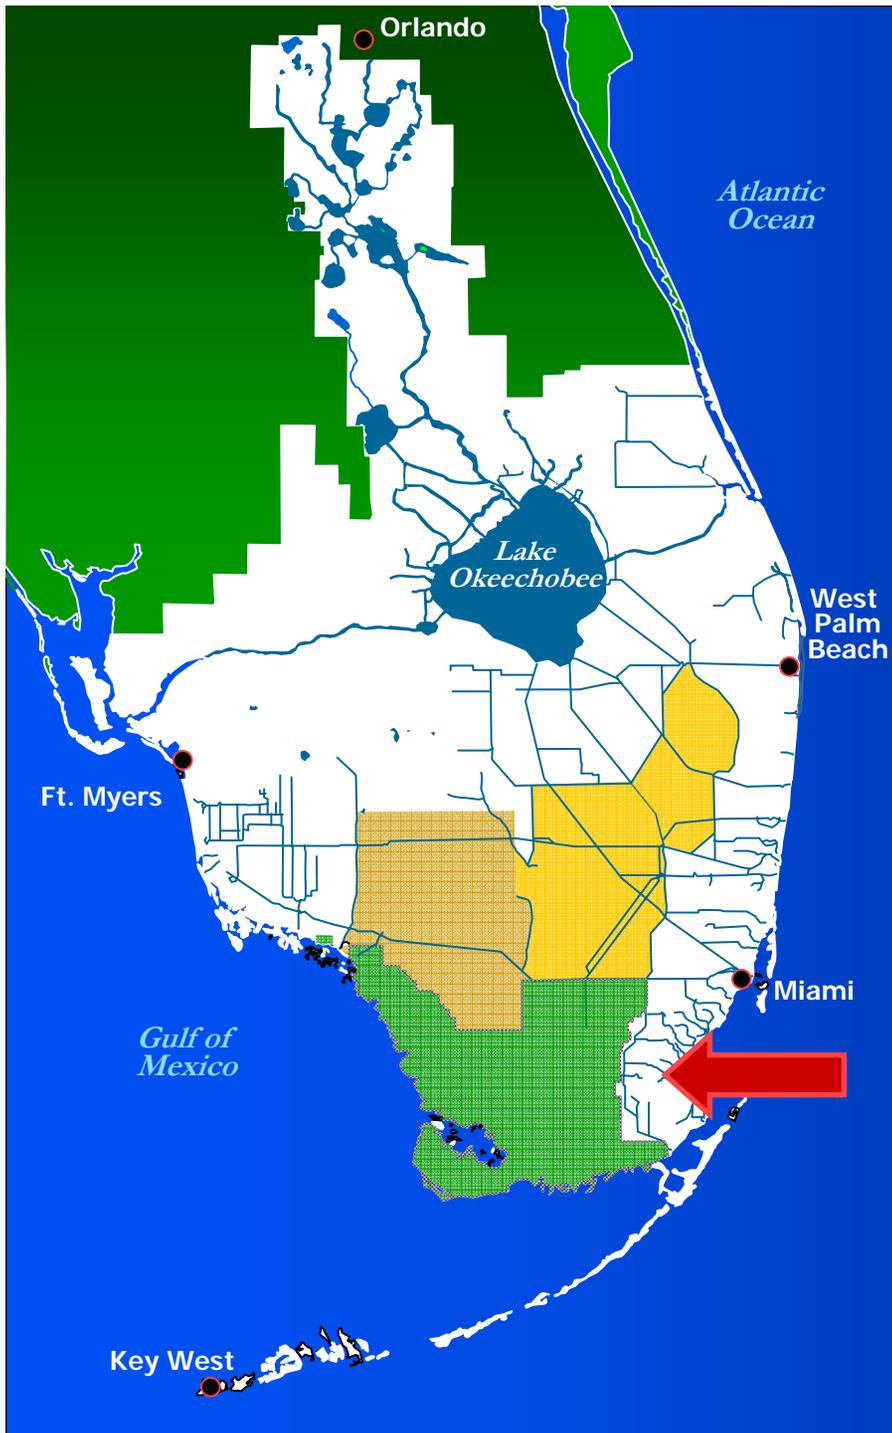


**C-111 South Dade
Project Location**

1994 C-111 GRR PLAN

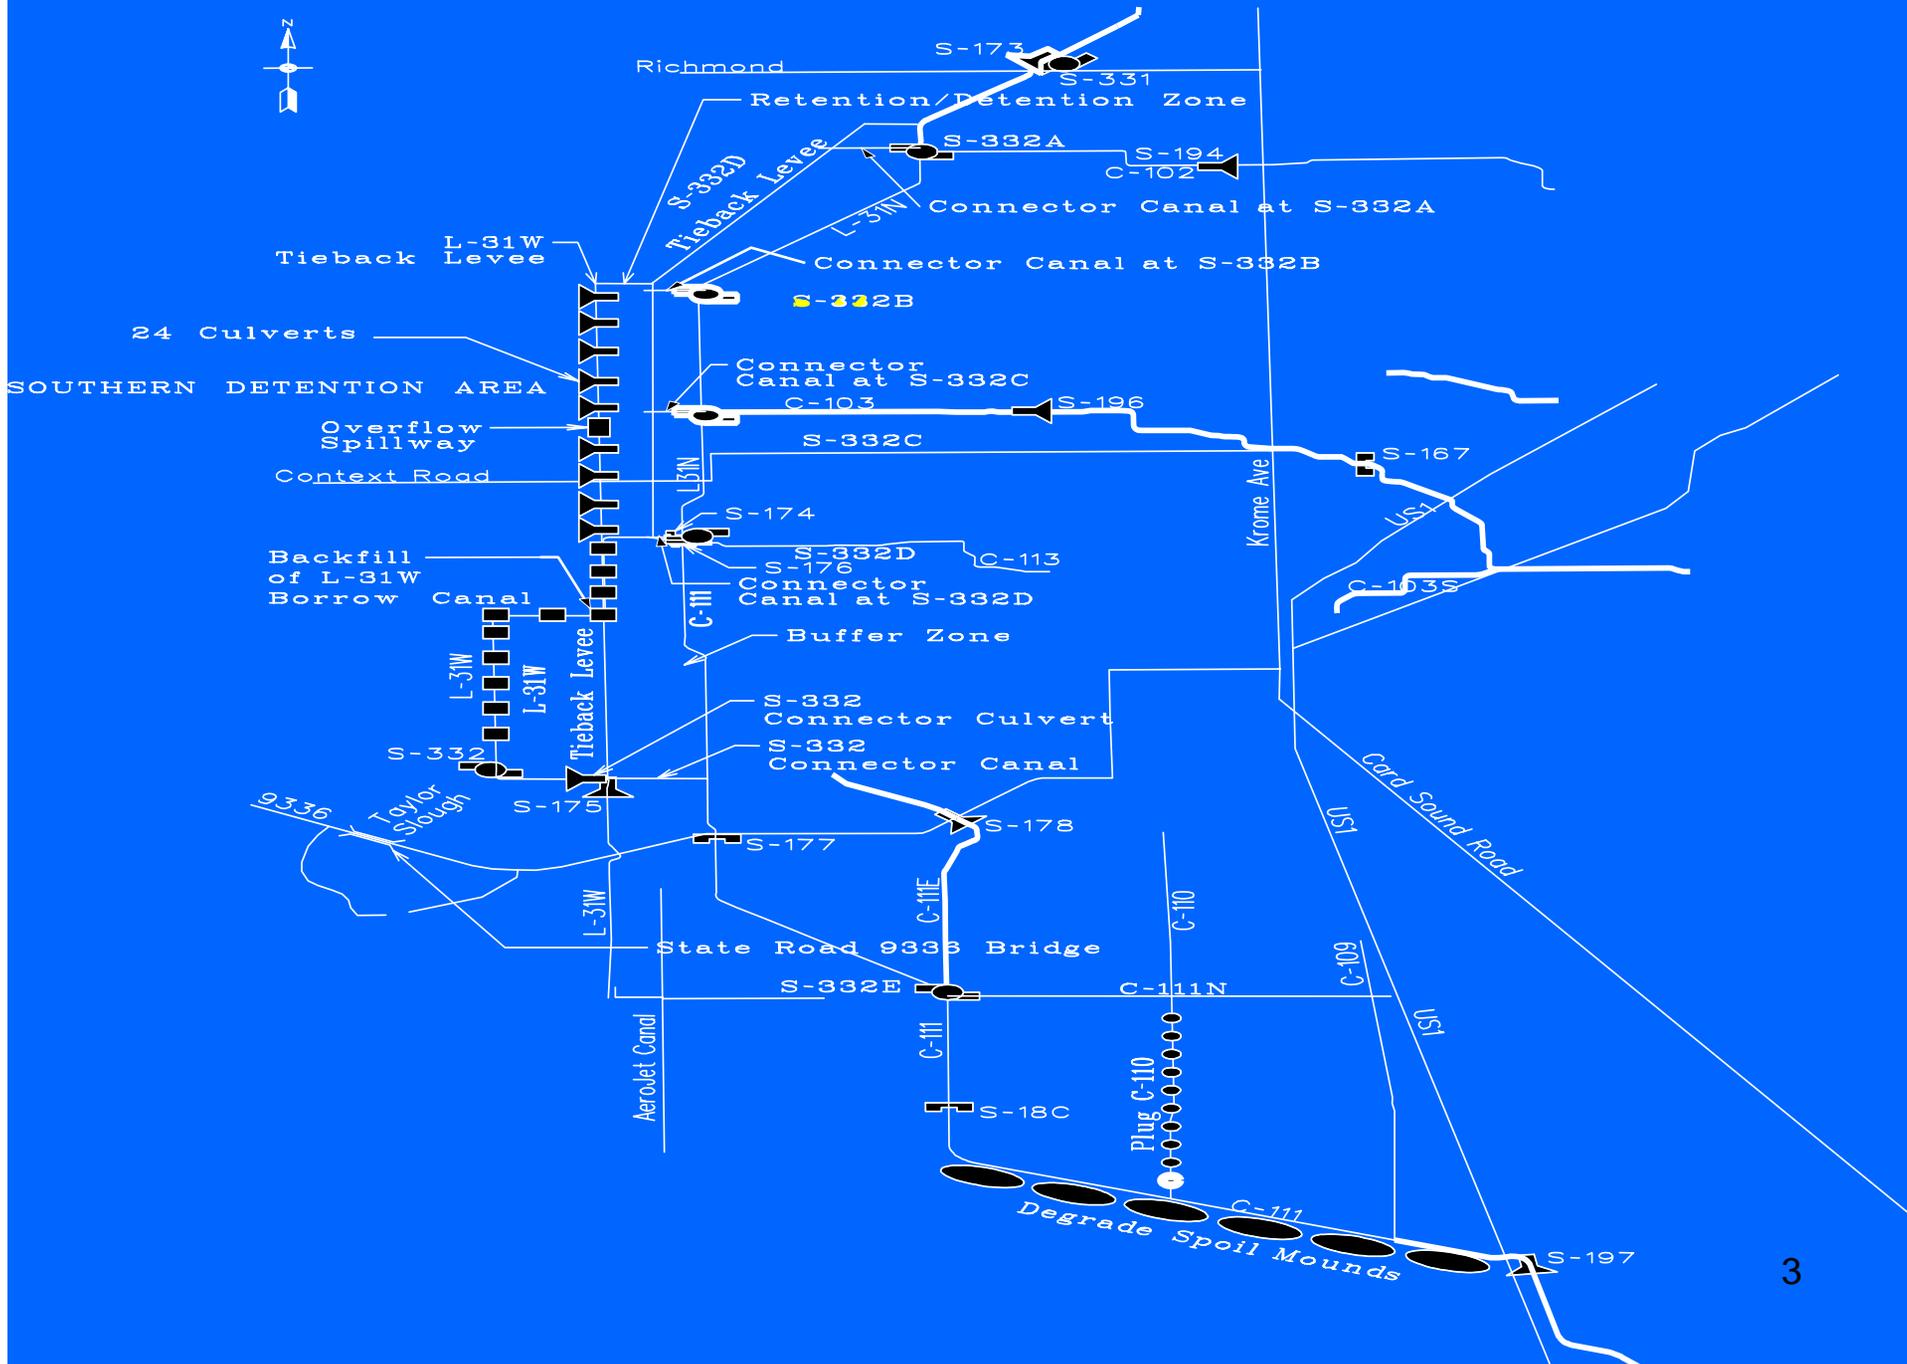

C-111 EDR

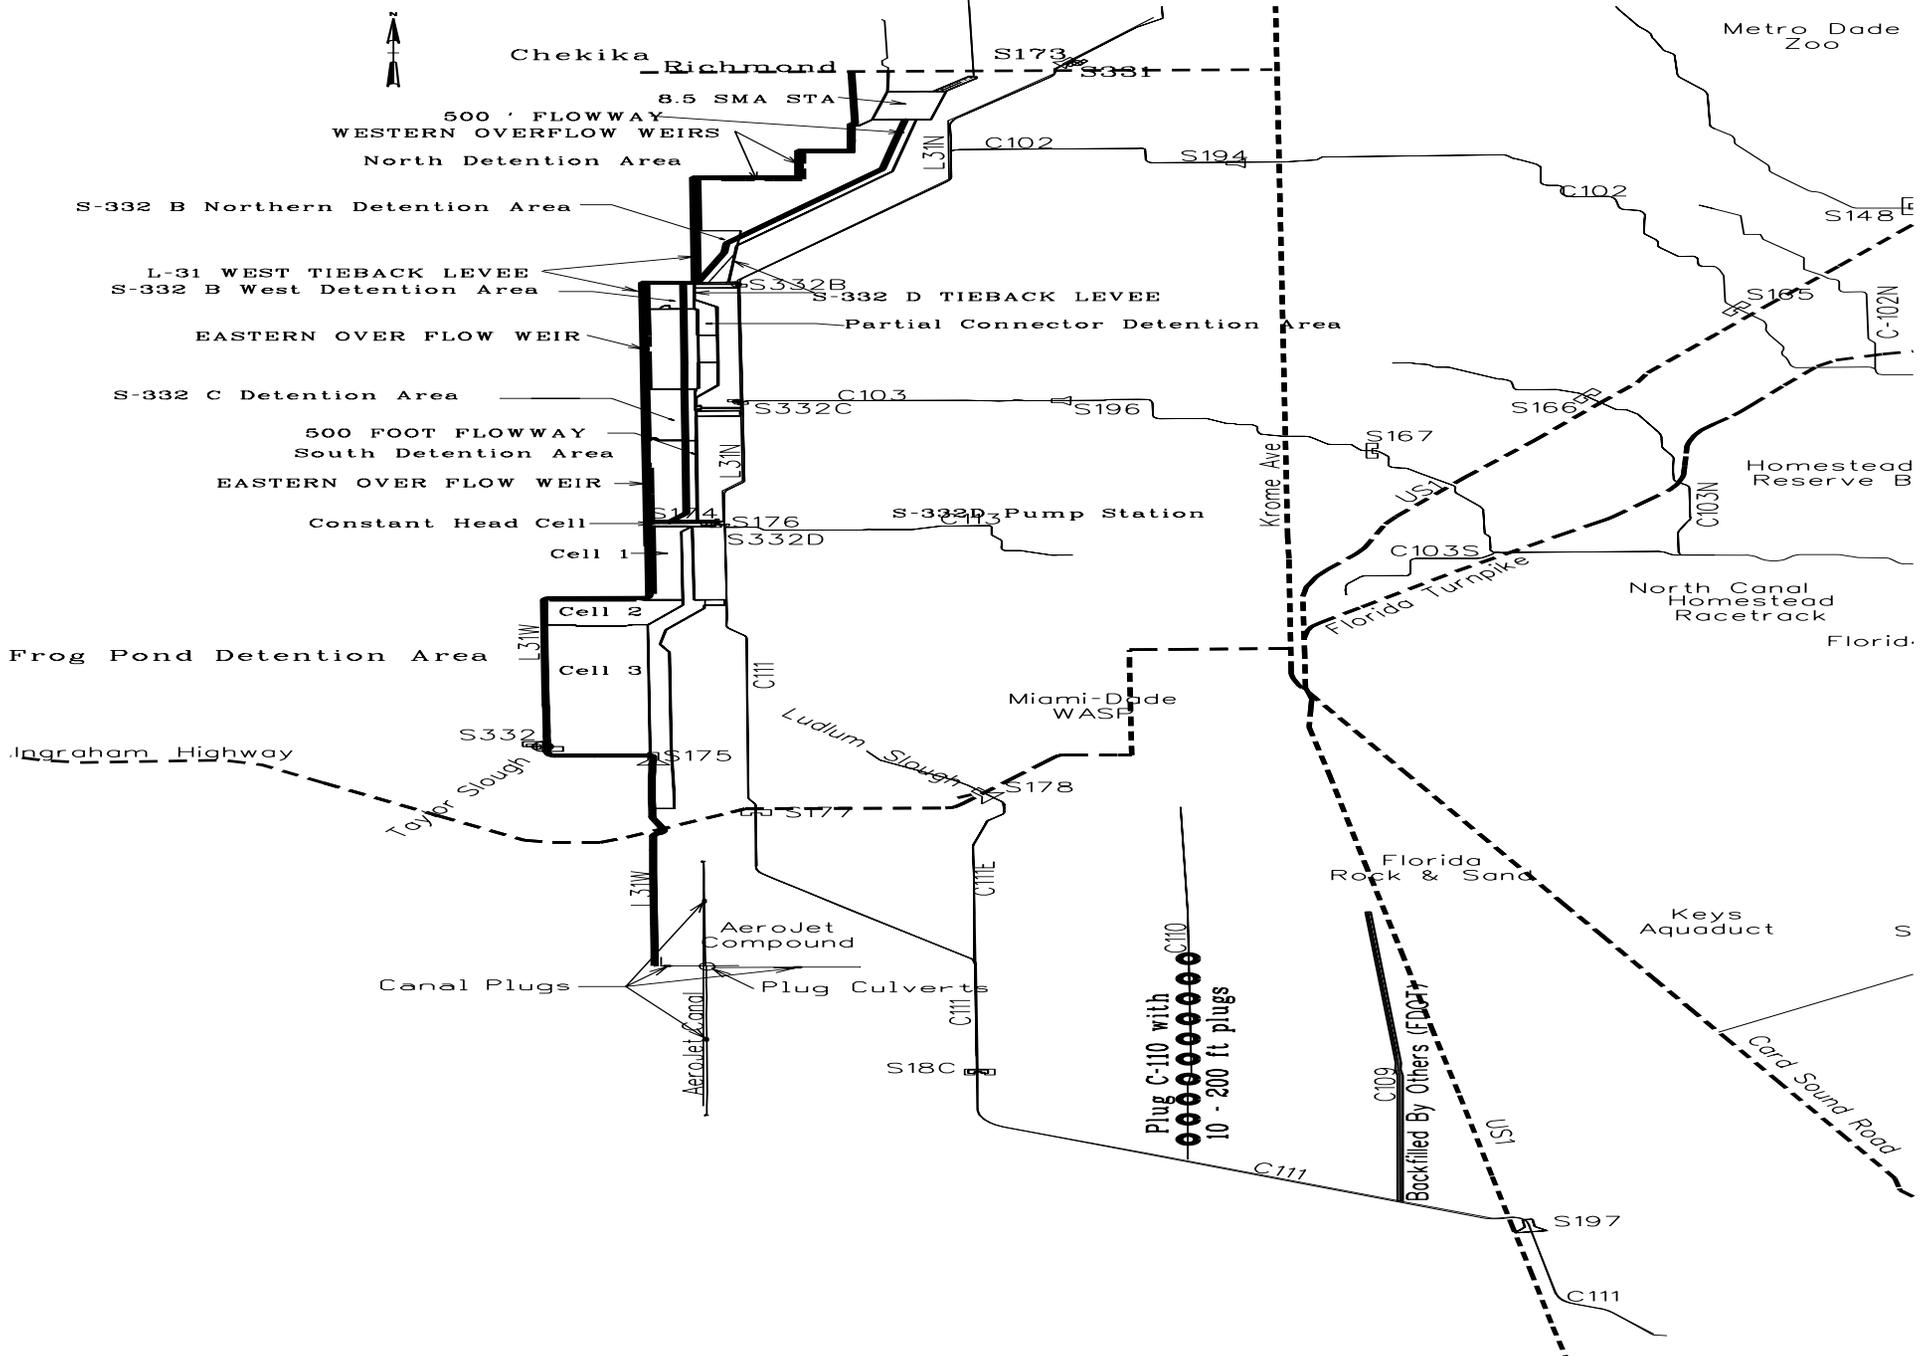

Project Objectives

- Restoration of the ecosystem in Taylor Slough and the eastern panhandle of ENP, enhance water deliveries to ENP, and maintain existing level of service for flood damage reduction
- 1994 GRR Recommended:
 - Replace SR 9336 bridge crossing to increase spatial distribution of flow
 - Construct 5 pump stations to:
 - Pump water from L-31N to ENP
 - Pump water from C-111/C-111E to a spreader canal (this is now part of the C-111 SC Project)
 - Construct L-31W Tieback Levee, L-31W Borrow Canal, S-332D Tieback Levee, Discharge Canals, S-332 Pump Station Connector Canal, and Nine Canal Plugs in C-109 and C-110
 - Construct the C-111N Spreader Canal (this is now part of the C-111 SC project)

Project Construction Status

- C-111 South Dade is being constructed under 11 different contracts
 - Contracts 1-5 are complete
 - Contracts 6 and 7 are under construction
 - Contracts 8-11 have not been awarded
- Lessons learned and implementation strategy have required design refinements for contracts 8-11

Project Construction Issues

- Contracts 8-11 can not be awarded until the design refinements have been approved
- An Engineering Documentation Report was drafted to:
 - Define design refinements
 - Obtain approval of the design refinements
 - Obtain approval of the change in total project cost
- HQ and SAD were presented the EDR on 14 Nov 2007
 - Comments and tasks were provided to SAJ
 - The District in the process of responding to the tasks
 - Upon completion of the tasks the District will require document submittal guidance from HQ and SAD
- WRDA 1996 changed the cost sharing responsibilities of the Federal and non-Federal sponsor
 - A PCA amendment is needed, but can not be drafted until the EDR is accepted and approved
 - The approved EDR will be used as the reference for the PCA amendment

Project Milestones

- Complete construction of contracts 6 and 7
 - Contract 6 estimated completion date is mid 2008
 - Contract 7 estimated completion date is Apr 08
- Receive approval of the EDR
 - This is the critical path of the project schedule
 - Delay of acceptance and approval of the design refinements delays the start and finish dates of contracts 8-11
- Advertise, award, and construct contracts 8-11
 - Start and Finish dates of contracts
 - Contract 8: Apr 08 – Apr 09
 - Contract 9: Oct 08 – Oct 09
 - Contract 10: Oct 09 – Apr 11
 - Contract 11: Oct 10 – Apr 12
 - Contracts 8-11 can not be awarded until approval of the EDR is obtained
