

**USACE/SAJ**

**SOUTH FLORIDA ECOSYSTEM  
RESTORATION PROJECT BRIEF**

**USACE – Jacksonville District**



# TAMIAMI TRAIL

- **Construction Progress = 34%**
- **Updated Completion Date = December 2013**
- **Major Features of Work Ongoing**
  - MOT – Maintenance of traffic
  - Pile driving & splicing
  - Earthwork
  - Concrete casting
  - Drainage
  - Roadway – Starting November 2011



# Progress Photos at 34%



Print #110726169  
Date: 07/26/11  
Lat/Lon: 25.7616 -80.514669  
Aerial Photography, Inc. 954-568-0484

SR 90 Tamiami Trail

**Kiewit**  
Infrastructure Group

ct

# Picayune Strand Restoration Construction Schedule

Faka Union Excavation




- Phase 1 – Prairie Canal and Phase I Road Removal (Aug 2006 - Sep 2007)
- Phase 2 – Merritt Pump Station and Phase II Road Removal (Sep 2009 - Aug 2012)
- Phase 3 – Faka Union Pump Station and Phase III Road Removal (Nov 2010 - Jul 2013)
- Phase 4 – Miller Pump Station and Phase IV Road Removal (Nov 2012 - Sep 2015)
  - Phase 5 – Protection Features (Mar 2012 - Mar 2013)



# C-44 Reservoir/STA Project

Three USACE contracts to be solicited and constructed over a seven year period:

- **Contract 1:** Includes the intake canal and project access road, & the Citrus Boulevard Bridge
  - Awarded in July 2011
- **Contract 2:** Construction of the reservoir, pump station and discharge canal
  - Planned for award in 2013
- **Contract 3:** Construction of the STA cells
  - Planned for award in 2016

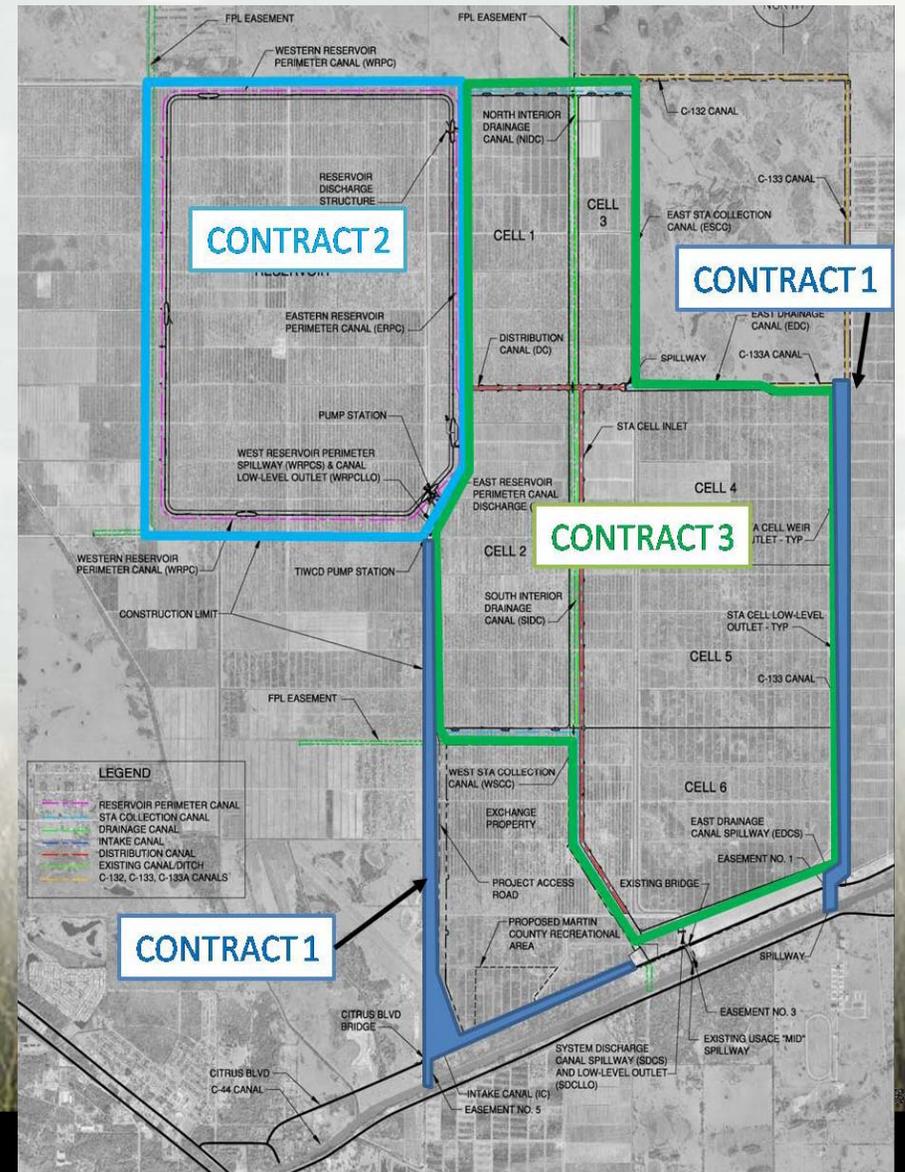

# KISSIMMEE RIVER

- **General Evaluation Report (GRR)**
  - FY2013 Approval
- **Award of 4 construction contracts in FY11**
  - S-67 Erosion Repair
  - Reach 2/3 Oxbow Dredging
  - S-65d Boat Ramp
  - S-69 Weir – To be awarded in FY11
- **Award of 2 construction contracts in FY12**
  - S-65E Spillway
  - Reach 3 Backfill – 2.2 miles of backfill
- **Award last construction contract in FY13**
- **Construction physically complete Dec 2014**





Afternoon storms begin to build over Lake Tohopekaliga

July 7, 2011

