


**South Florida
Ecosystem
Restoration
Update**

restoration
restoration

Working Group

October 2006

South Florida Everglades Ecosystem Restoration Program

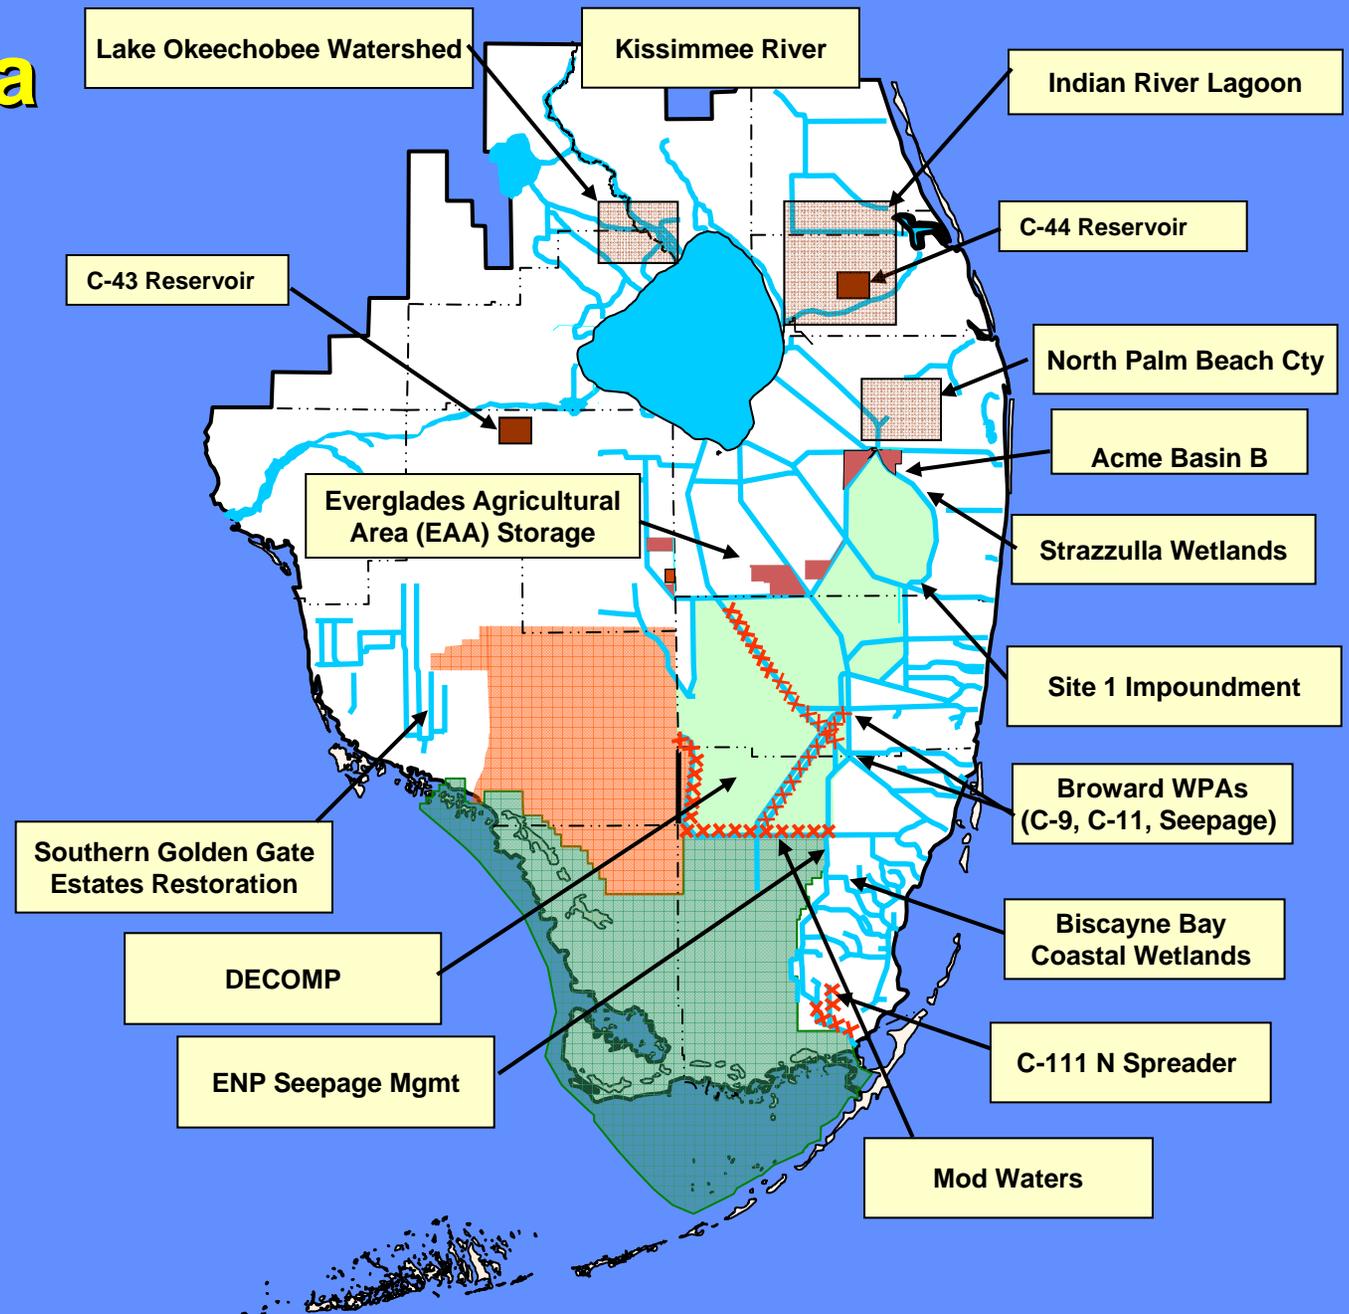

Accomplishments Last 90 Days

- 5 Year report submitted to Congress
- Lake Okeechobee Regulation Schedule Study – Draft SEIS posted 18 Aug, Public Meetings held in Sept, comment period extended 2 weeks from 2 Oct
- 17 Workshops/meetings held on Master Recreation Plan
- Initiated startup operations for Lake Okeechobee Critical projects, Taylor Creek and Nubbin Slough STA's

Accomplishments Last 90 Days (Cont'd)

- The final PIR for Site 1 has been released for State and Agency review
- C-111 (C&SF) – Awarded S-331 Command Bldg
- Permit issued for A8 project for Picayune Strand Road Removal
- Conducted Independent Technical Review of HHD repair, report posted on Jax District website. Started replacement of Bench cut

Accomplishments Last 90 Days (Cont'd)

- Awarded Seminole Big Cypress Contract
- Awarded contract for Istokpoga Canal Improvements (Kissimmee)
- Construction continues on second Kissimmee Backfill contract, media day held on 6 and 13 Oct
- Completed 30% Design of C-23/24 STA of IRL-S
- CERP Reset

Accomplishments Next 90 Days

- **Chief's Report for Site 1**
- **Completion of construction of PSTA field test work at STA 1E, initiate operations**
- **Complete Interim Goals and Targets Agreement (get signed)**
- **Complete Guidance Memoranda**
- **Complete LORSS EIS and Water Control Plan**

Accomplishments Next 90 Days

- Complete final PIR/EA for Broward WPA
- Complete special assessment of Bold Decomp and present to Task Force
- Permit decisions expected for Temporary Forward pumps, Nubbin Creek STA Expansion, and Taylor Creek reservoir Test cell.
- Complete AFB Packages for C-111 SC Biscayne Bay, Lakes Park to HQ
- FSM Package for ENP Seepage Mgmt

Accomplishments Next 90 Days

- **Herbert Hoover Dike Repair**
 - **Complete restoration of Bench and initiate Toe Drain repair**
 - **Continue redesign of Rehab work**

Major Events Scheduled for FY 07

- Mod Waters – Completion of 8.5 SMA contract, April 07. Design completion of Tamiami Trail modifications. Contract for construction to award in late 2007.
- EAA – Revised Draft PIR to incorporate larger STA into project and revised water budget analysis. Final PIR in Summer 07.
- C-111 SC – Draft PIR in Summer 07
- C-43 – Complete Draft PIR in Spring 07
- Biscayne Bay Coastal Wetlands – Draft PIR in Summer 07

Major Events Scheduled for FY 07

- CSOP – Approval of SEIS and Water Control Plan in Summer 07
- HDD - Reinitiate Rehab work and Complete 2nd MRR and Award 2nd rehab Contract
- Kissimmee River – Award 3rd Backfill Contract
- C-111 (C&SF) – Award contract for Detention Basins
- C-51/STA 1E – Initiate PSTA Field Test and Award L-40 modification contract.

Major Events Scheduled for FY 07

- **Initiate Comprehensive Water Quality Feasibility Study**
- **Southwest Florida Feasibility Study – TSP Selection**
- **ASR Regional Study – Interim Report in Spring 07**

Questions?

