



**South Florida  
Ecosystem  
Restoration  
Program and Projects  
Update**

**Task Force Meeting  
October 1, 2009**

restoration  
restoration

# Progress on Program Level Activities

- CERP land crediting policy change approved
- CERP Master Agreement executed on August 13
- Design Agreement Amendment 2 executed on August 13
- Pre-Project Crediting Agreements executed on August 13:
  - Picayune Strand
  - Indian River Lagoon – South
  - C-111 Spreader Canal
  - Biscayne Bay Coastal Areas
  - C-43 West Basin Storage Reservoir

# Kissimmee River Restoration




- Contract 11A – S-65DX1 Retrofit: Awarded on Sept 10 for \$1.664M
- Contract 15 – River Acres Flood Protection: Bids opened Sept 10. Contract award scheduled by end of Sept.
- Contract 2B1 – C37 Enlargement (ARRA funding): Scheduled for Jan 2010 award
- CNT 6A1B – S-68 Spillway Additions): Construction physically complete
- Relocation agreement with CSX Railroad executed
- Post Authorization Change Report scheduled for completion in March 2010

# Modified Water Deliveries to ENP




- Tamiami Trail: Contract awarded to Kiewit Southern on Sept 25 for \$81M
- Engineering Design Report (EDR) and Supplemental EIS for conveyance and seepage features scheduled for completion in FY 10
- Swale pilot project scheduled for installation in FY 10, pending results of modeling
- Combined Operational Plan (COP) effort underway

# Picayune Strand Restoration

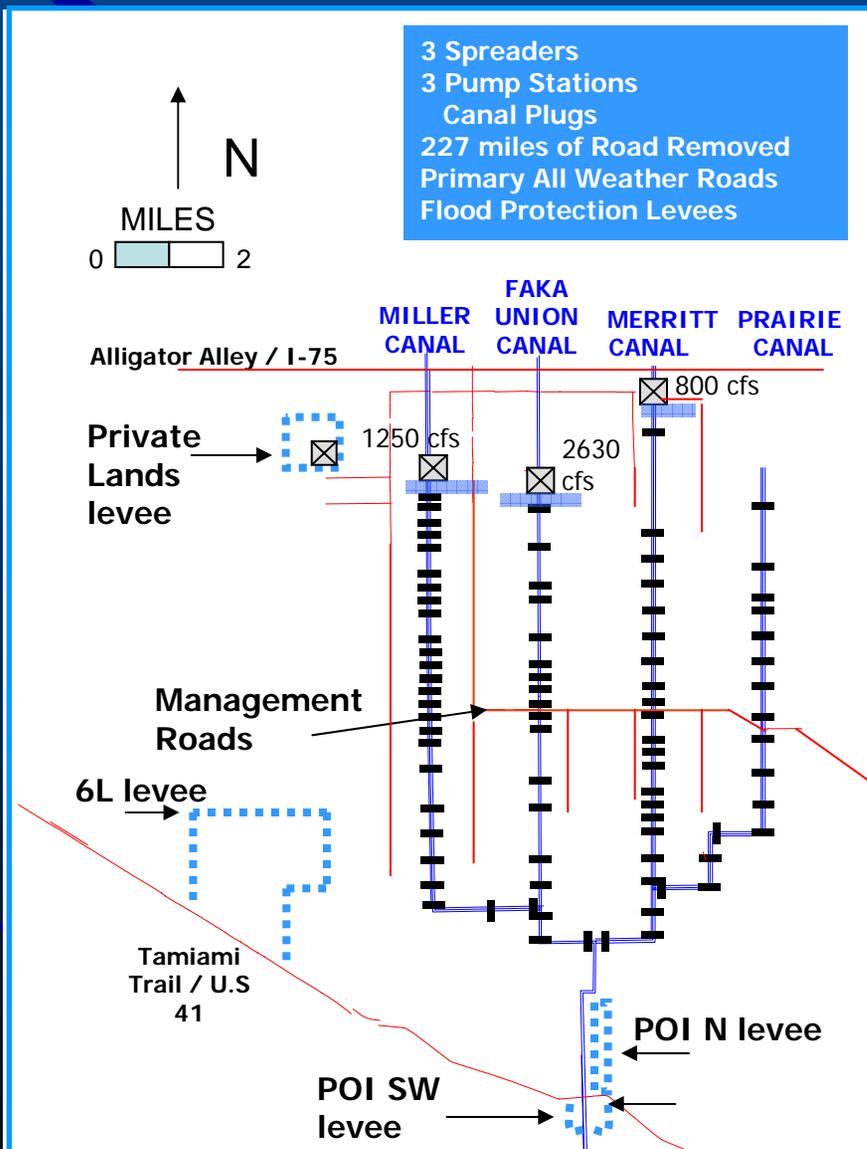


- Project Partnership Agreement executed Aug 13
- Merritt Canal Pump Station/Road Removal Contract: Advertised on Aug 6; Bids scheduled to be opened Oct 2; Contract award scheduled by Oct 29
- Faka Union Canal/Road Removal Contract: Plans & Specs conversion to be awarded by end of Sept; Construction contract award scheduled for late FY 10

# Everglades Restoration Transition Plan (ERTP) – Phase I

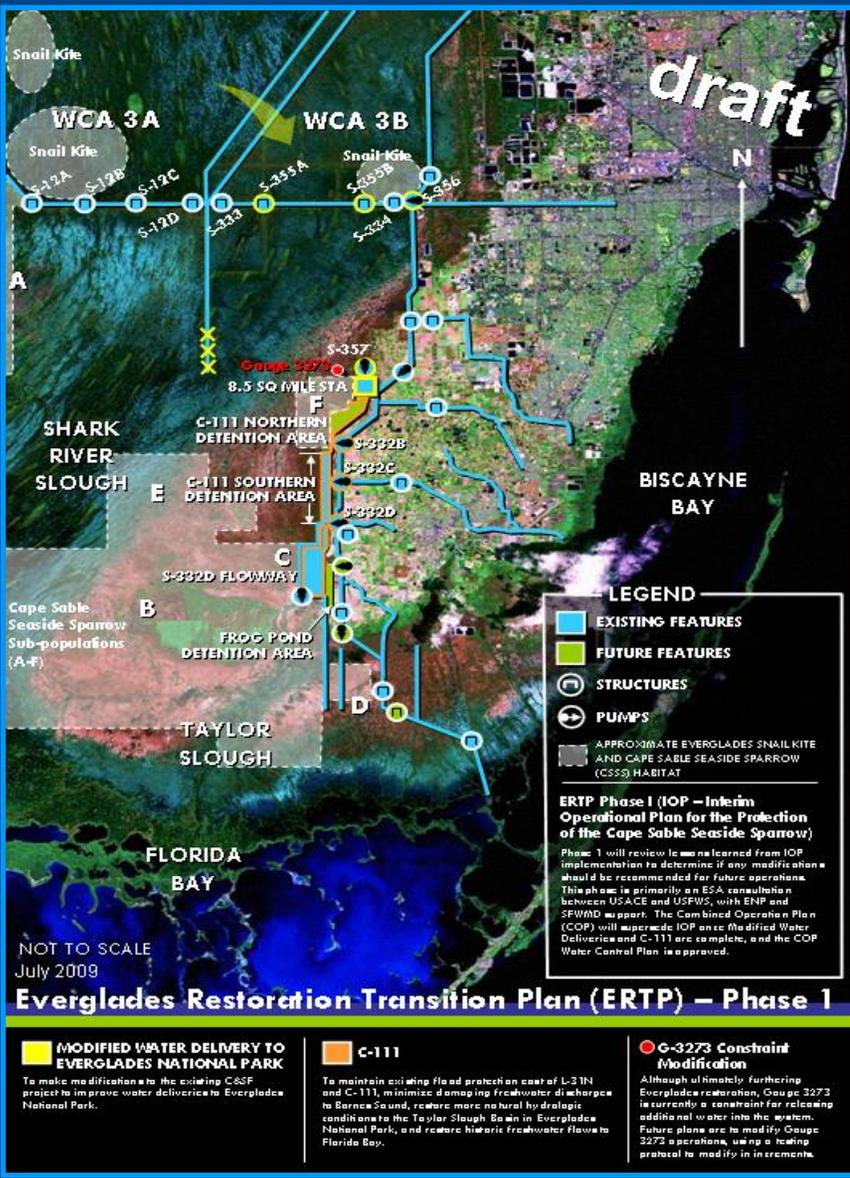


- The Biological Opinion (BO) for the Interim Operational Plan (IOP) expires October 2010
- Consultation with FWS underway to maximize operational flexibilities to improve species and habitat conditions while maintaining C&SF project purposes during the transition to Everglades restoration
- Corps Biological Assessment scheduled to be transmitted to FWS March 2010
- FWS scheduled to complete Biological Opinion July 2010

# C-43 West Basin Storage Reservoir

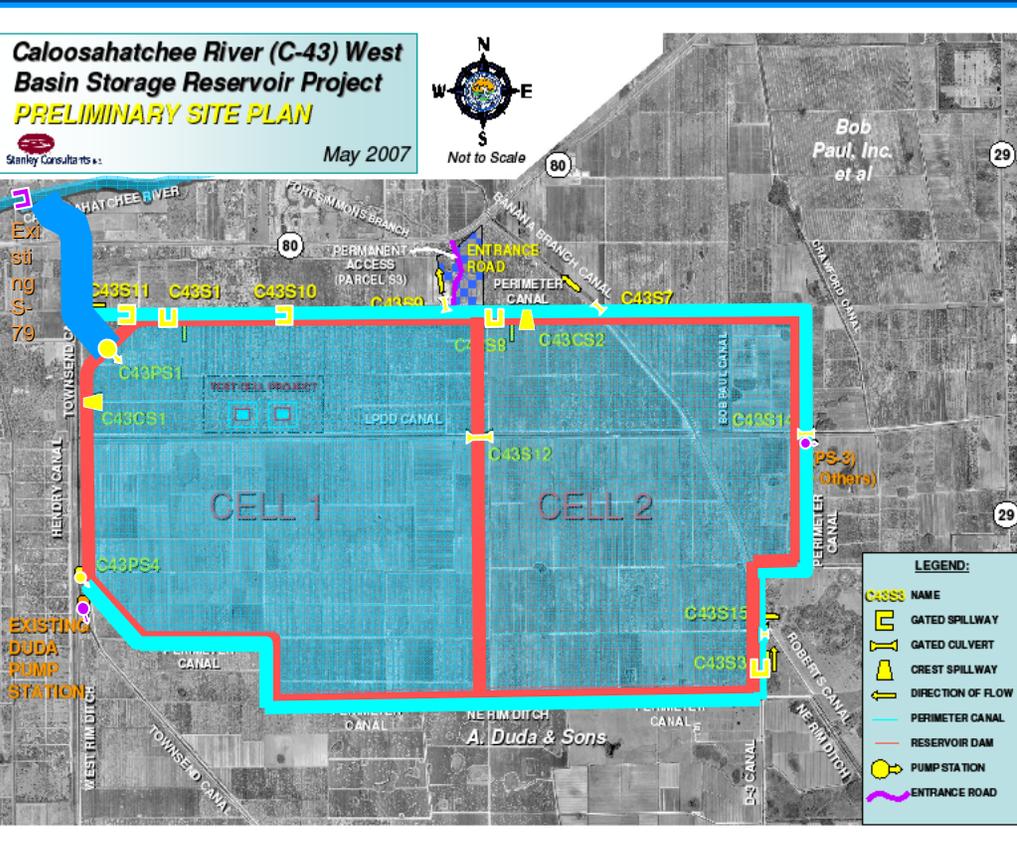


- Real estate appraisals for PIR being updated in accordance with land crediting policy change
- Final PIR Addendum scheduled to be submitted early Nov
- Chief of Engineers Report scheduled to be completed in Jan 2010
- PIR scheduled for submission to Congress in Aug 2010

# C-111 Spreader Canal – Design Test

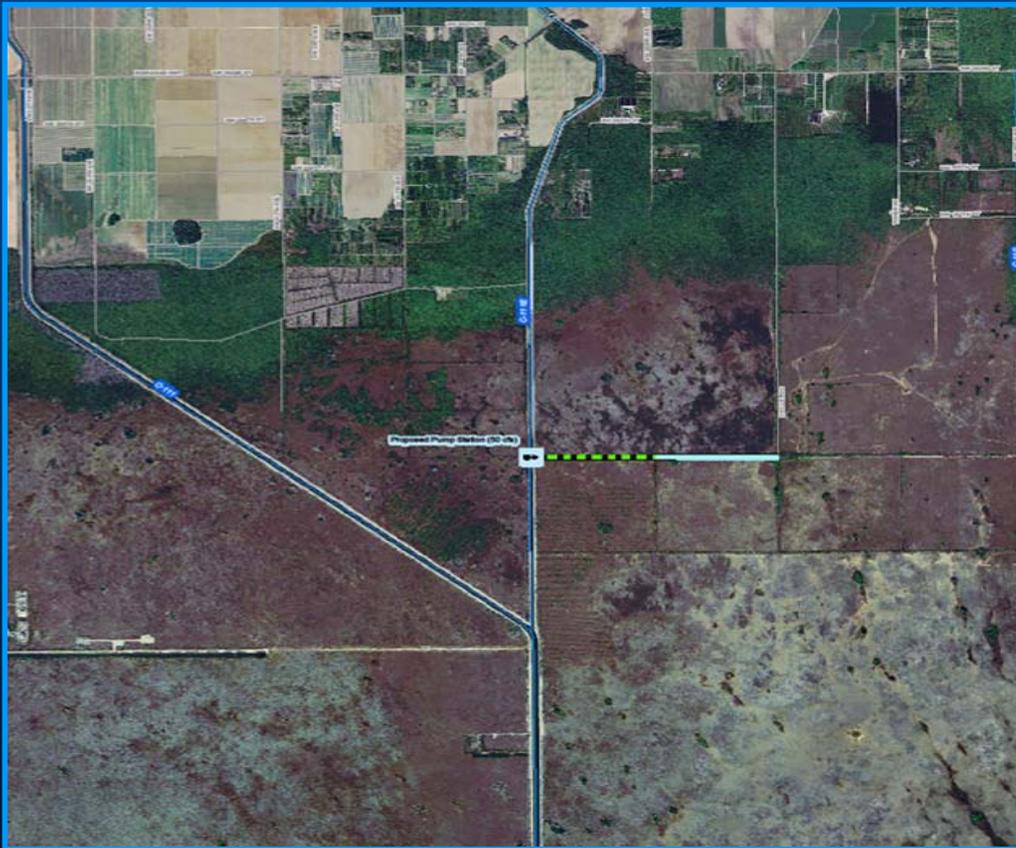


- **Features:** 1 mile spreader canal and 50 cfs pump
- Test of pump and spreader canal effectiveness
- Contract awarded Sept 1 for \$2.4M to ZFI Engineering & Construction

# C-111 Spreader Canal – PIR

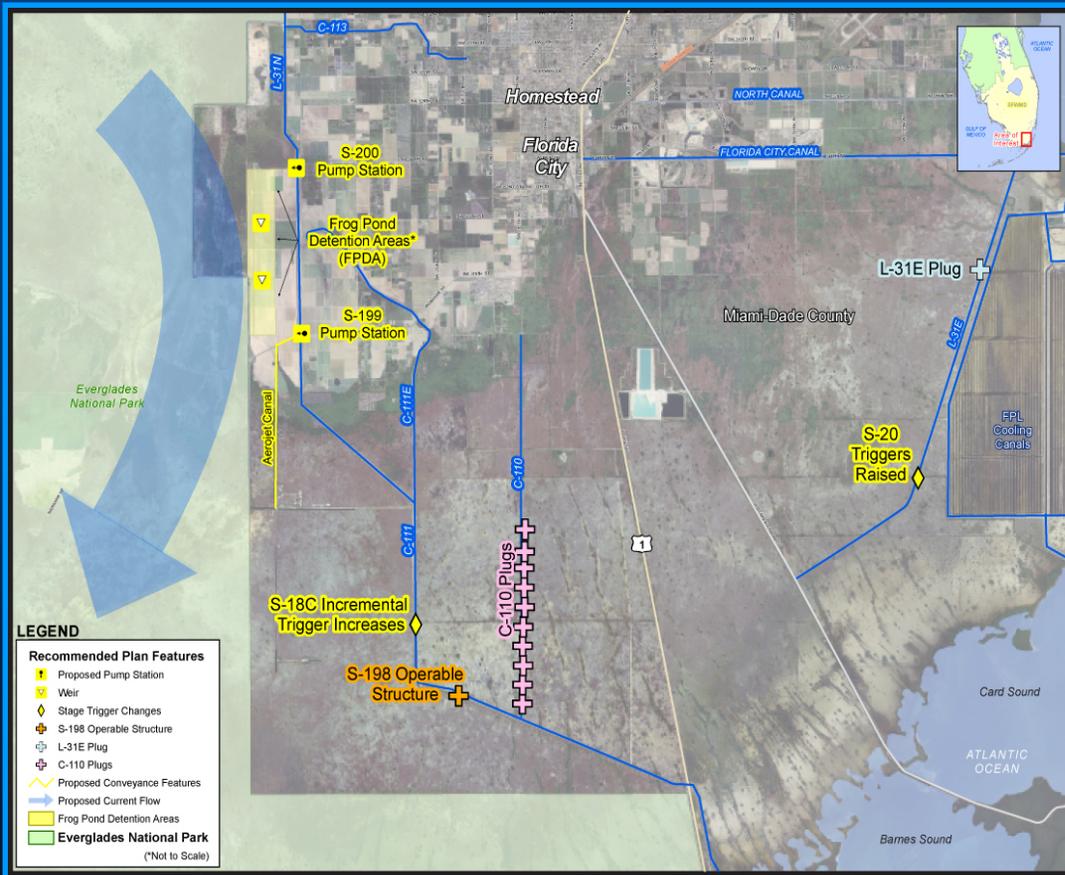


- Real estate appraisals for PIR being updated in accordance with land crediting policy change Final PIR scheduled to be submitted to HQ in Nov 9
- Civil Works Review Board briefing scheduled for Dec 15
- Chief of Engineers Report scheduled for Apr 2010
- PIR scheduled for submission to Congress Oct 2010

# Biscayne Bay Coastal Wetlands

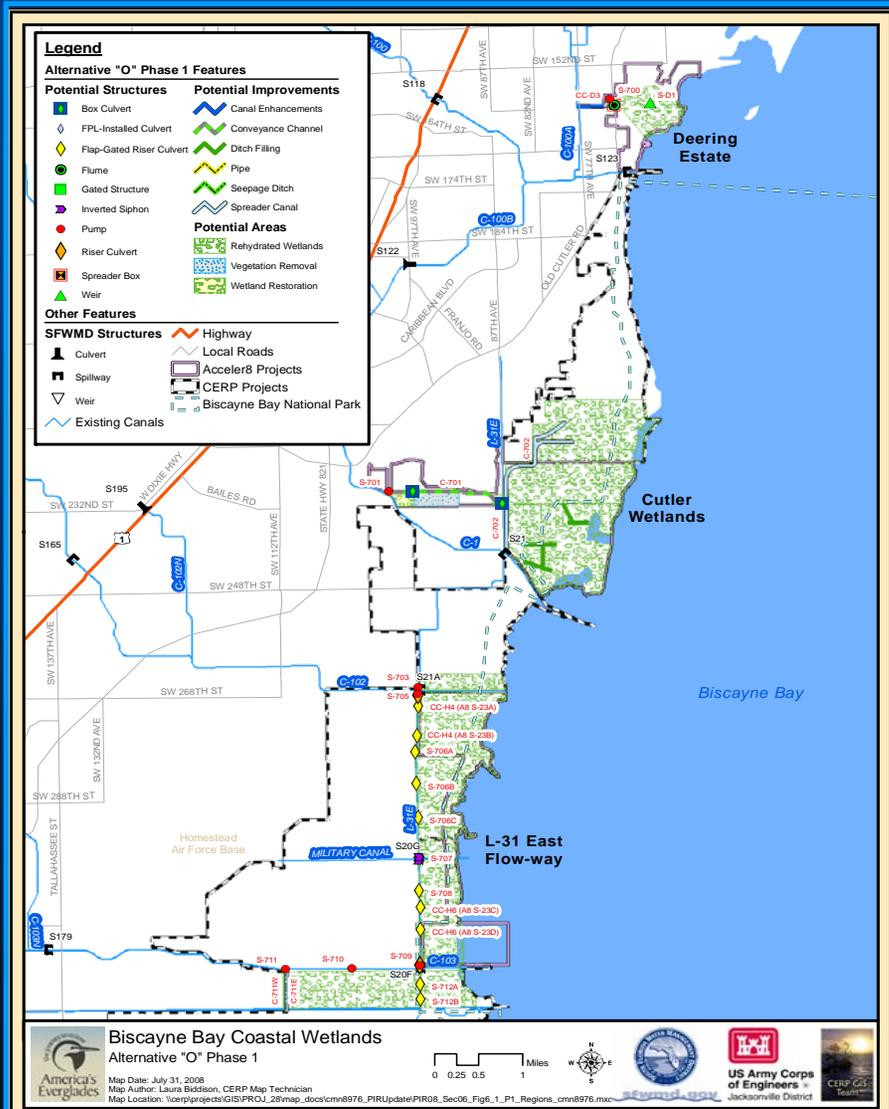


- Real estate appraisals for PIR being updated in accordance with land crediting policy change
- Draft PIR scheduled for public release in Nov
- Chief of Engineers Report scheduled for Aug 2010
- PIR submission to Congress scheduled for Feb 2011

# Broward County Water Preserve Areas

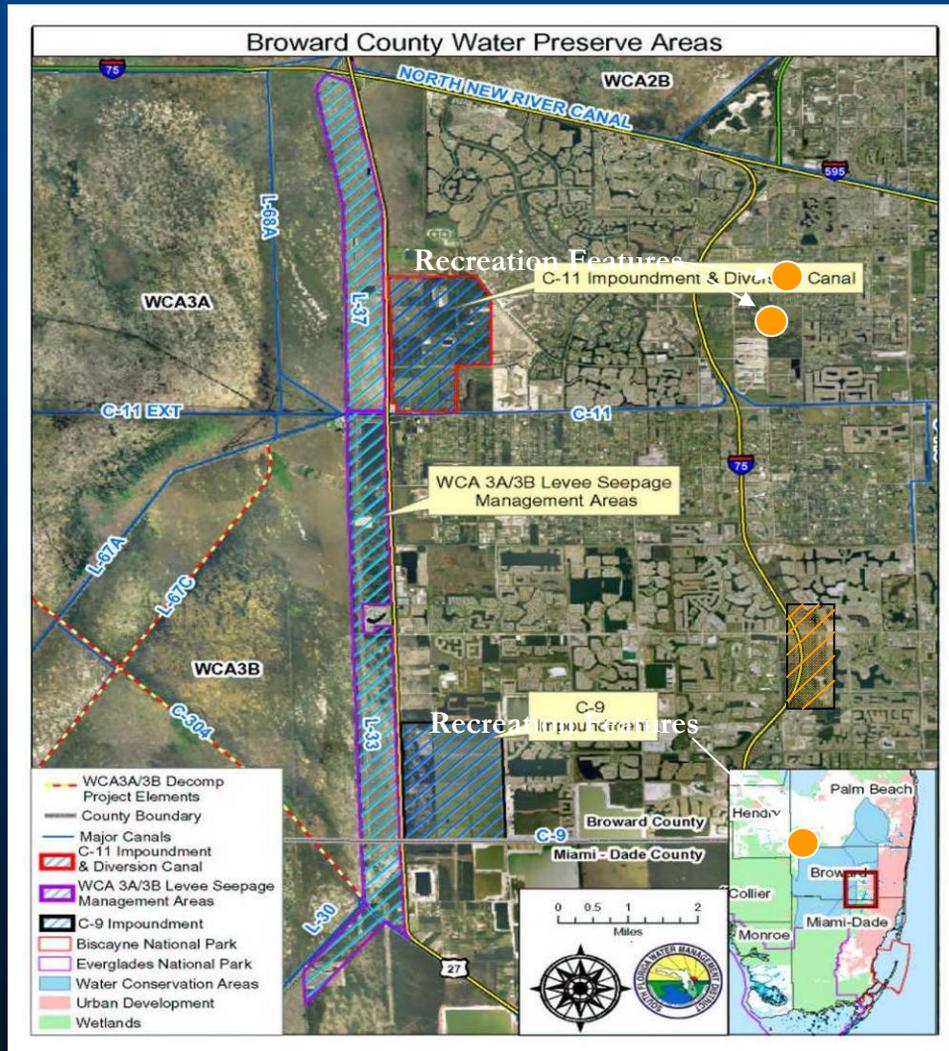

- Real estate appraisals for PIR being updated in accordance with land crediting policy change
- Report schedule to be determined after development of PIR completion strategy

# Herbert Hoover Dike Rehabilitation

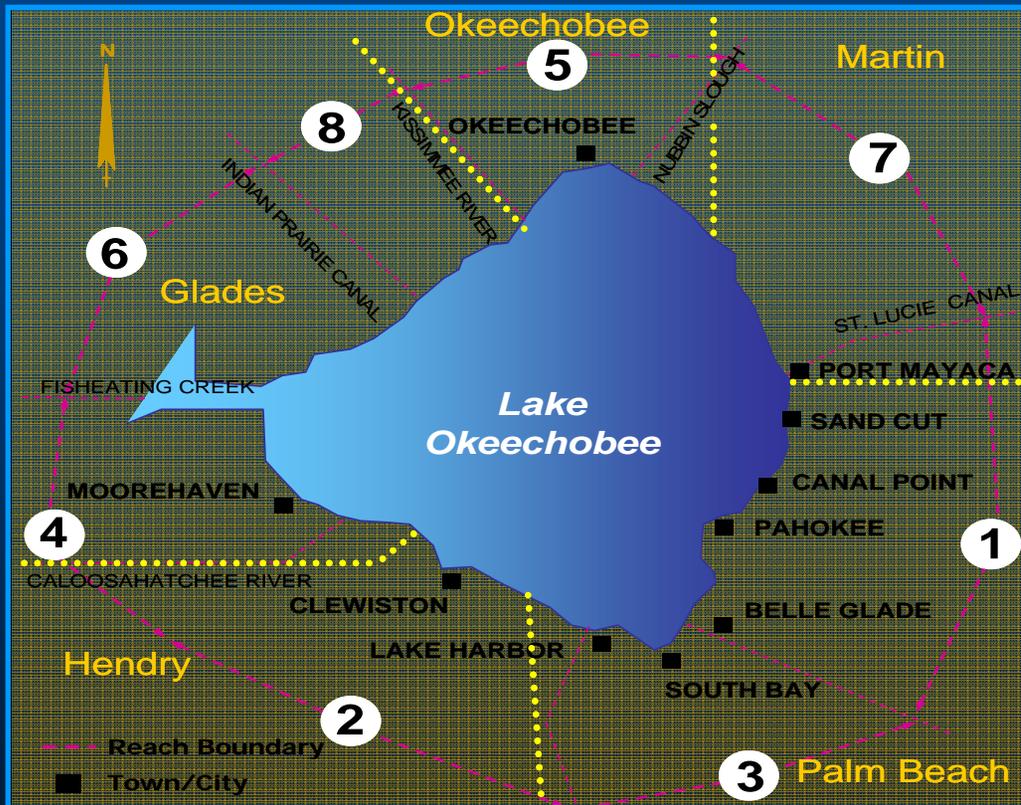

- Three task orders for cut-off wall construction underway in Reach 1
- Reach 1-D quarry fill contract awarded in Aug; contractor has commenced clearing and grubbing
- Three cut-off wall task orders Reinforces 143 miles of levee surrounding Lake Okeechobee
- Plans and specs for culvert 14 and cut-off wall task order 5 nearing completion for award in FY 10

**Questions?**

