




# **Acceler8 Update**

**Kenneth G. Ammon, P.E.  
Deputy Executive Director  
CERP Resource Area**

**Working Group Meeting  
West Palm Beach, Florida  
August 30, 2005**



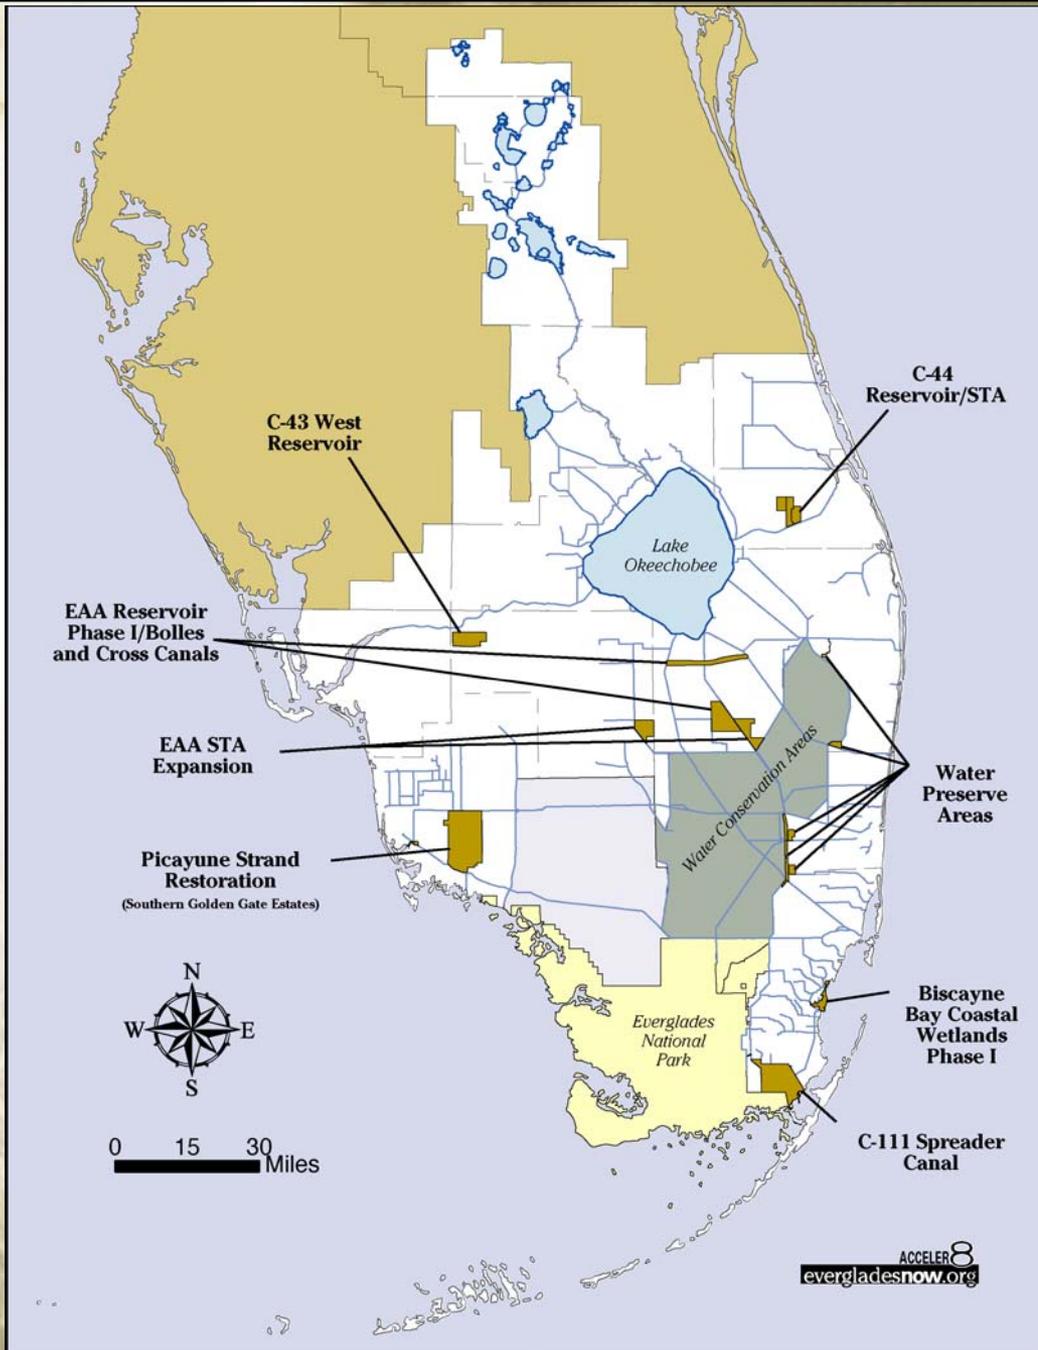

# Acceler8 Project Location Map

# Acceler8 Updated Status Report

## Annual Work Plan Status

### ■ Outlook 4<sup>th</sup> Quarter

- Initiate Design Phase for Pump Stations - Picayune Strand
- Complete C-43 Test Cell Design and Construction Documents
- Initiate Final Design for STA 2 - Cell 4, STA 5 – Flowway 3 & STA 6 – Section 2
- Complete BODR on Site 1 and Acme Basin B Projects
- EAA A1 Reservoir CM@Risk Solicitation

# Ongoing Activities – August 2005

## ■ EAA Reservoir

- Reviewing Draft BODR

## ■ STA 2, Cell 4;

- Reviewing 60% Plans & Specs
- Receive 90% Plans & Specs (Aug 22)

## ■ STA 5, Flowway 3

- Reviewing 60% Plans & Specs

## ■ STA 6, Section 2

- Reviewing 60% Plans & Specs

## ■ C-43

- Test Cell Design

## ■ Biscayne Bay Coastal Wetlands

- Receive Survey



# Upcoming Activities – September 2005

## ■ ACME Basin B – Canal & Pump Station

- 30% Plans & Specs

## ■ STA 6, Section 2

- 90% Plans & Specs

## ■ STA 5, Flowway 3

- 90% Plans & Specs

## ■ C-111 Spreader Canal

- Survey

## ■ Site 1 Impoundment

- BODR
- Survey



# Upcoming Activities – October 2005

## ■ Water Preserve Areas

### ■ C-9 Impoundment

- Interim Design Report

### ■ C-11 Impoundment

- Interim Design Reports

### ■ WCA 3B Levee Seepage Management

- Interim Design Report

## Schedule Issues

### ■ Picayune Strand

#### ■ Post-PIR modeling required by USF&W

- Threatened delaying site work

#### ■ Acceler8 Team implementing schedule recovery plan

- Initiate design of Pumping Stations
- Evaluating modeling alternatives w/ USACE
- Could impact construction deadlines established with USACE & USFWS (Woodley-Albright Letter)

## Schedule Issues (con't)

### ■ Water Preserve Areas

#### ■ Resource & Contracting issues delayed BODR development

- Threatened delay of construction start

#### ■ Acceler8 Team implemented schedule recovery plan

- Develop Interim Design Reports
  - In lieu of typical BODR
- Expect to meet construction deadlines established with USACE & USFWS (Woodley-Albright Letter)

# QUESTIONS
