

Comprehensive Everglades Restoration Plan

Restoration Program and Project Status

Working Group / Science Coordination Group Meeting
September 20, 2012

Howie Gonzales
Chief, Ecosystem Branch
USACE – Jacksonville District



®



BUILDING STRONG®

US ARMY CORPS OF ENGINEERS | JACKSONVILLE DISTRICT

CERP Implementation

1st Generation

- Indian River Lagoon – South (IRL-S)
- Picayune Strand Restoration Project
- Site 1 Impoundment

2nd Generation

- C-43 West Basin Storage Reservoir
- C-111 Spreader Canal Western Project
- Biscayne Bay Coastal Wetlands
- Broward County Water Preserve Area



Indian River Lagoon – South (IRL-S): C-44 Reservoir/STA



Contract 1:

- Features: Intake canal, project access road, Citrus Blvd. bridge
- Construction contract awarded July 2011
- Construction complete May 2014

Contract 2:


- Features: Reservoir, pump station, discharge canal
- Construction contract scheduled for award in 2014

Contract 3:

- Features: STA cells
- Construction contract scheduled for award in 2016



Picayune Strand Restoration Project

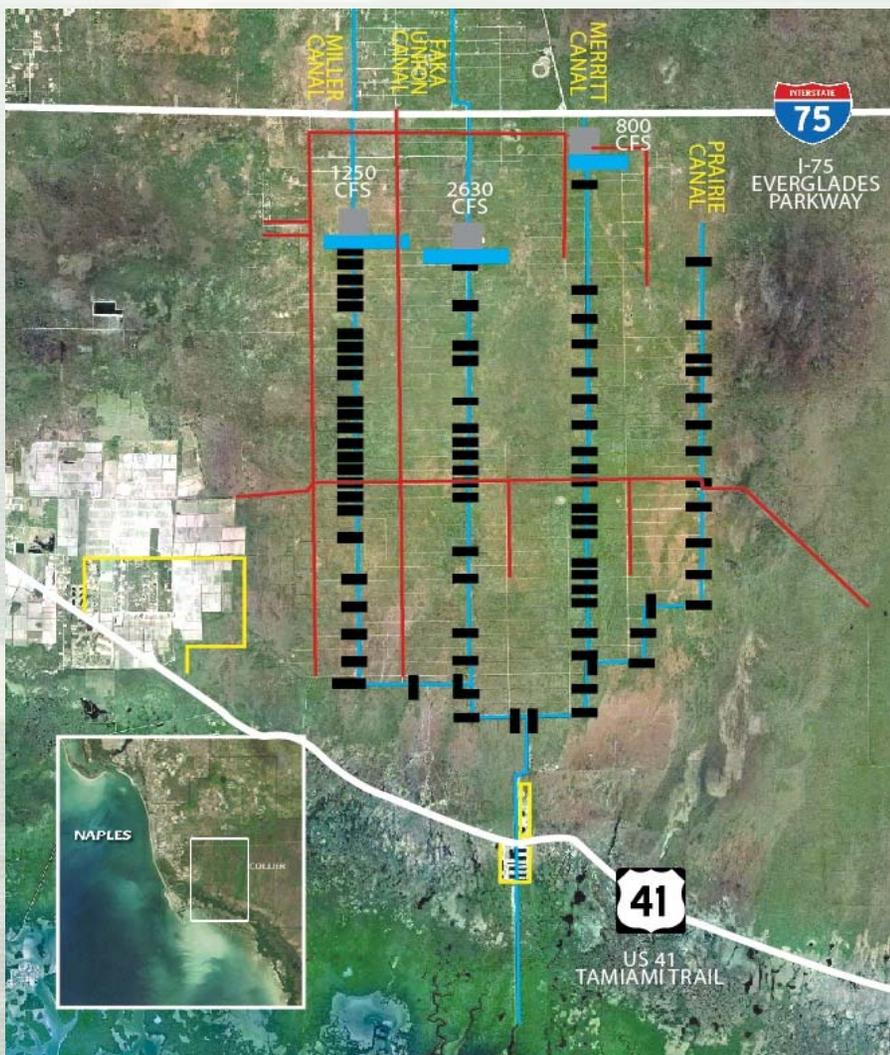

- **Merritt Pump Station and Road Removal**

- Testing & Commissioning Start: March 2013
- Canal Plugs Start: April 2013
- Operational Test & Monitoring: May 2013-May 2014

- **Faka Union Pump Station and Road Removal**

- Testing & Commissioning Start: March 2014
- Canal Plugs Start: April 2015
- Operational Test & Monitoring: May 2014-May 2015

- **Miller Union Pump Station and Road Removal**

- ATR/Sponsor Review of Final P&S: November 2012
- Contract Award: August 2013




Site 1 Impoundment

Phase 1:

- Features: D-525 Levee Enhancement; S-530 Spillway; Wildlife Wetland Area
- Construction contract awarded September 2010
- Status: Construction efforts on hold pending contractor issue resolution

Phase 2:

- Features: Inflow Pump Station; Seepage Pump Station; Discharge/Outflow Structures; New D-525 Embankment
- Status: Efforts on hold pending completion of Phase 1

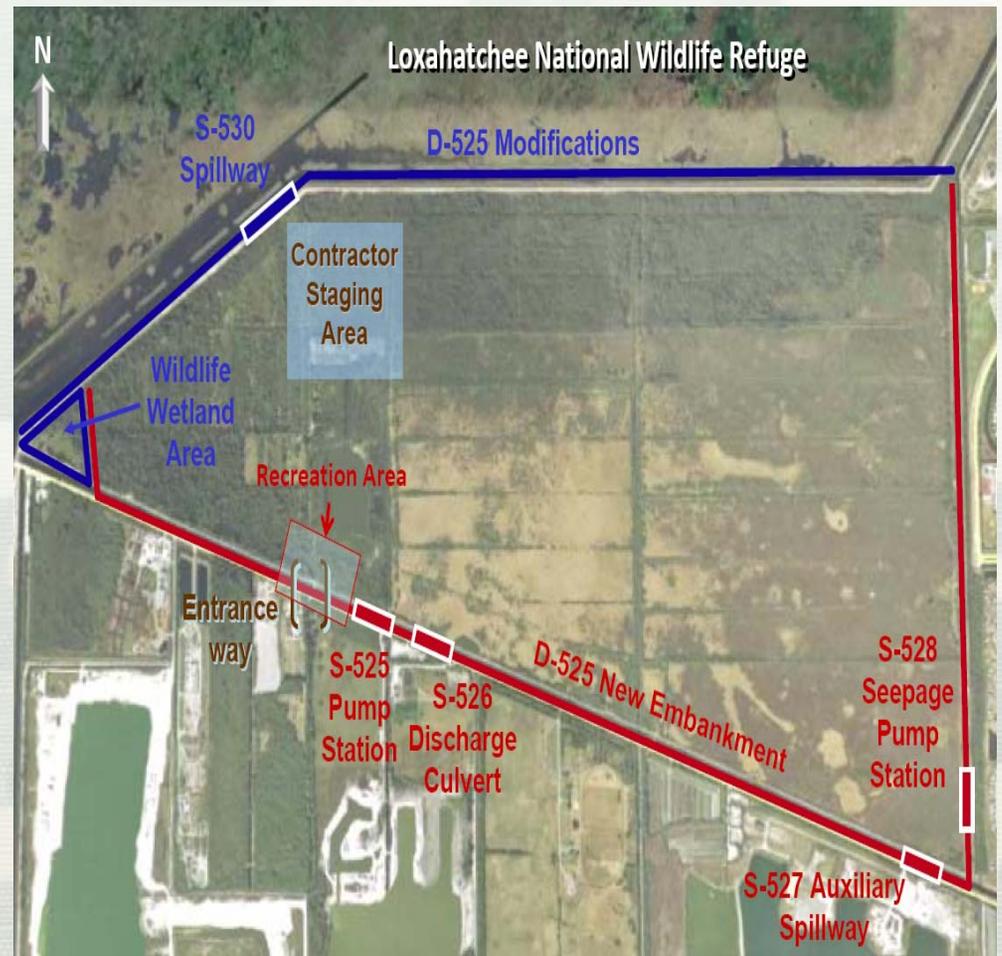

CERP Implementation

1st Generation

- Indian River Lagoon – South (IRL-S)
- Picayune Strand Restoration Project
- Site 1 Impoundment

2nd Generation

- C-43 West Basin Storage Reservoir
- C-111 Spreader Canal Western Project
- Biscayne Bay Coastal Wetlands
- Broward County Water Preserve Area



2nd Generation CERP Projects



C-43 West Basin Storage Reservoir

- Purpose = improve timing, quantity and quality of freshwater deliveries to Caloosahatchee River estuary
- Record of Decision signed and report submitted to Congress on April 13, 2011
- Awaiting Congressional Authorization and Appropriation

C-111 Spreader Canal

- Purpose = improve water deliveries to Florida Bay and to improve hydroperiods and hydroperiods in Southern Glades /Model Lands
- Record of Decision signed and report submitted to Congress on July 19, 2012
- Awaiting Congressional Authorization and Appropriation



S-199



2nd Generation CERP Projects




Biscayne Bay Coastal Wetlands

- Purpose = improve freshwater deliveries to Biscayne Bay
- Chief of Engineer's Report signed on May 2, 2012. Currently under review at OMB.
- ROD signature scheduled for October 2012.

Broward County Water Preserve Area

- Purpose to reduce seepage, recharge groundwater, provide water supply, prevent saltwater intrusion in western Broward County
- Chief of Engineer's Report signed on May 21, 2012. Currently under review at OMB.
- ROD signature scheduled for November 2012

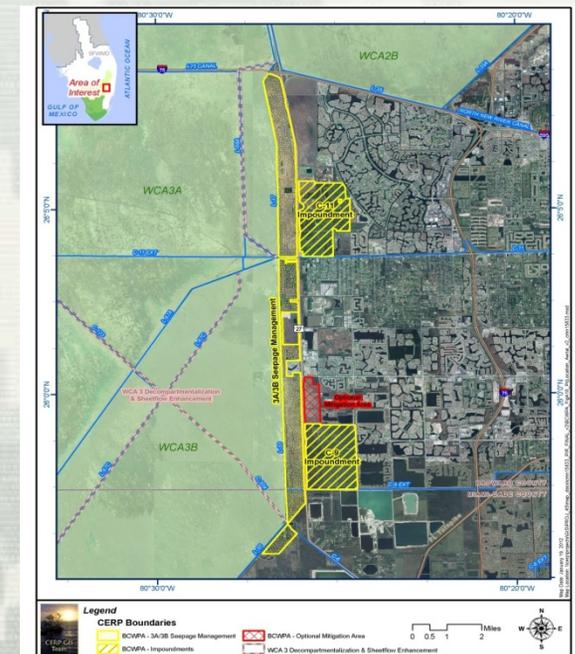

Comprehensive Everglades Restoration Plan

Restoration Program and Project Briefings

Questions?



®



BUILDING STRONG®

US ARMY CORPS OF ENGINEERS | JACKSONVILLE DISTRICT
