




Acceler8 Update

Joint Water Resource Advisory Commission and South Florida Ecosystem Restoration Task Force Meeting December 7, 2005

**Kenneth G. Ammon, P.E.
Deputy Executive Director, CERP**




Everglades Restoration Accelerated Projects

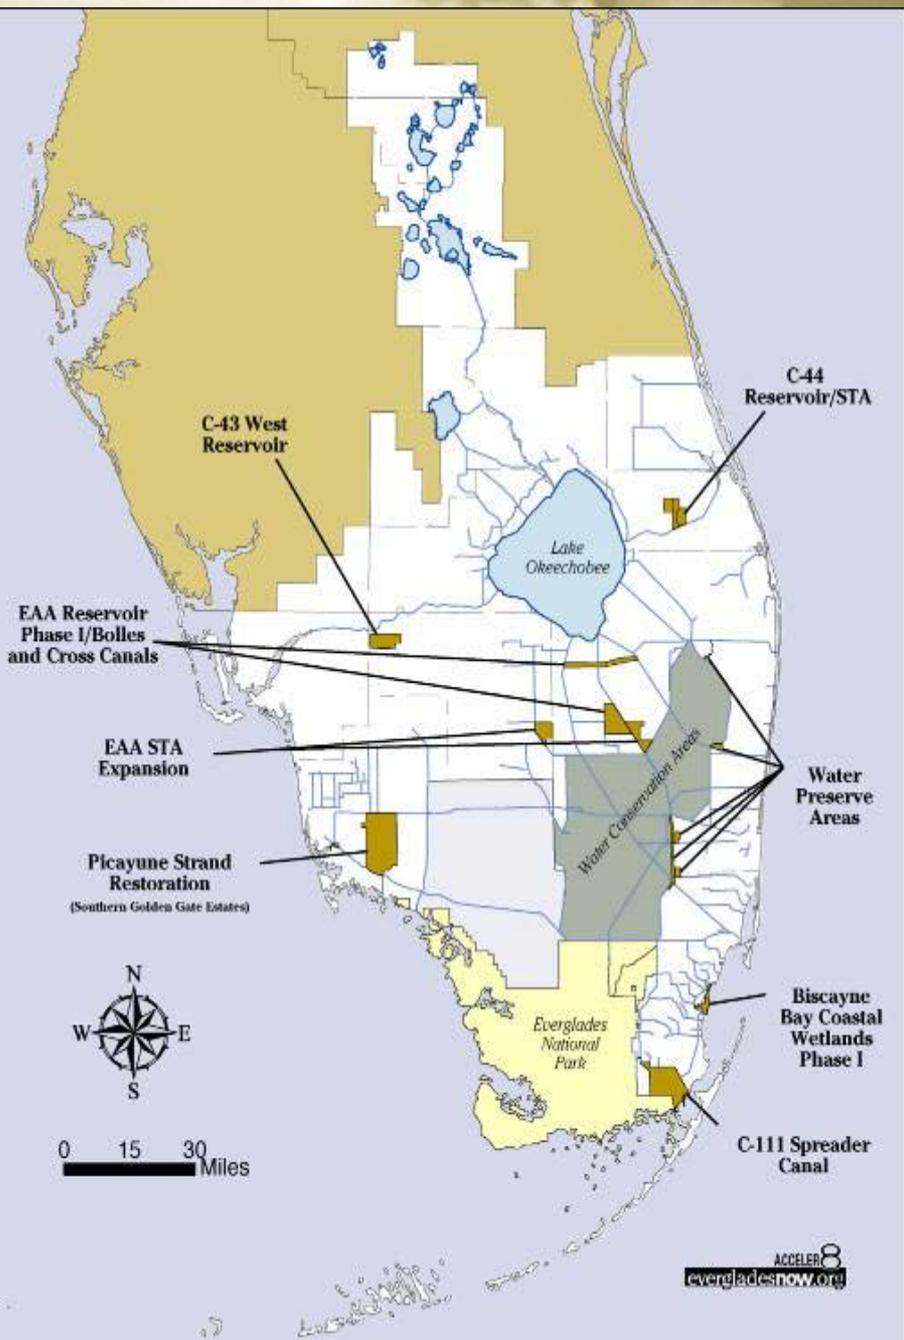


- C-43 (Caloosahatchee River) West Reservoir
- EAA Reservoir Phase I/Boles & Cross Canals
- EAA Stormwater Treatment Area Expansion
- Picayune Strand (Southern Golden Gate Estates) Restoration
- C-44 (St. Lucie Canal) Reservoir / STA
- Water Preserve Areas
- Biscayne Bay Coastal Wetlands Phase I
- C-111 Spreader Canal

Reservoir & STA's Storage Volume per Year
STA's depth: 4 ft

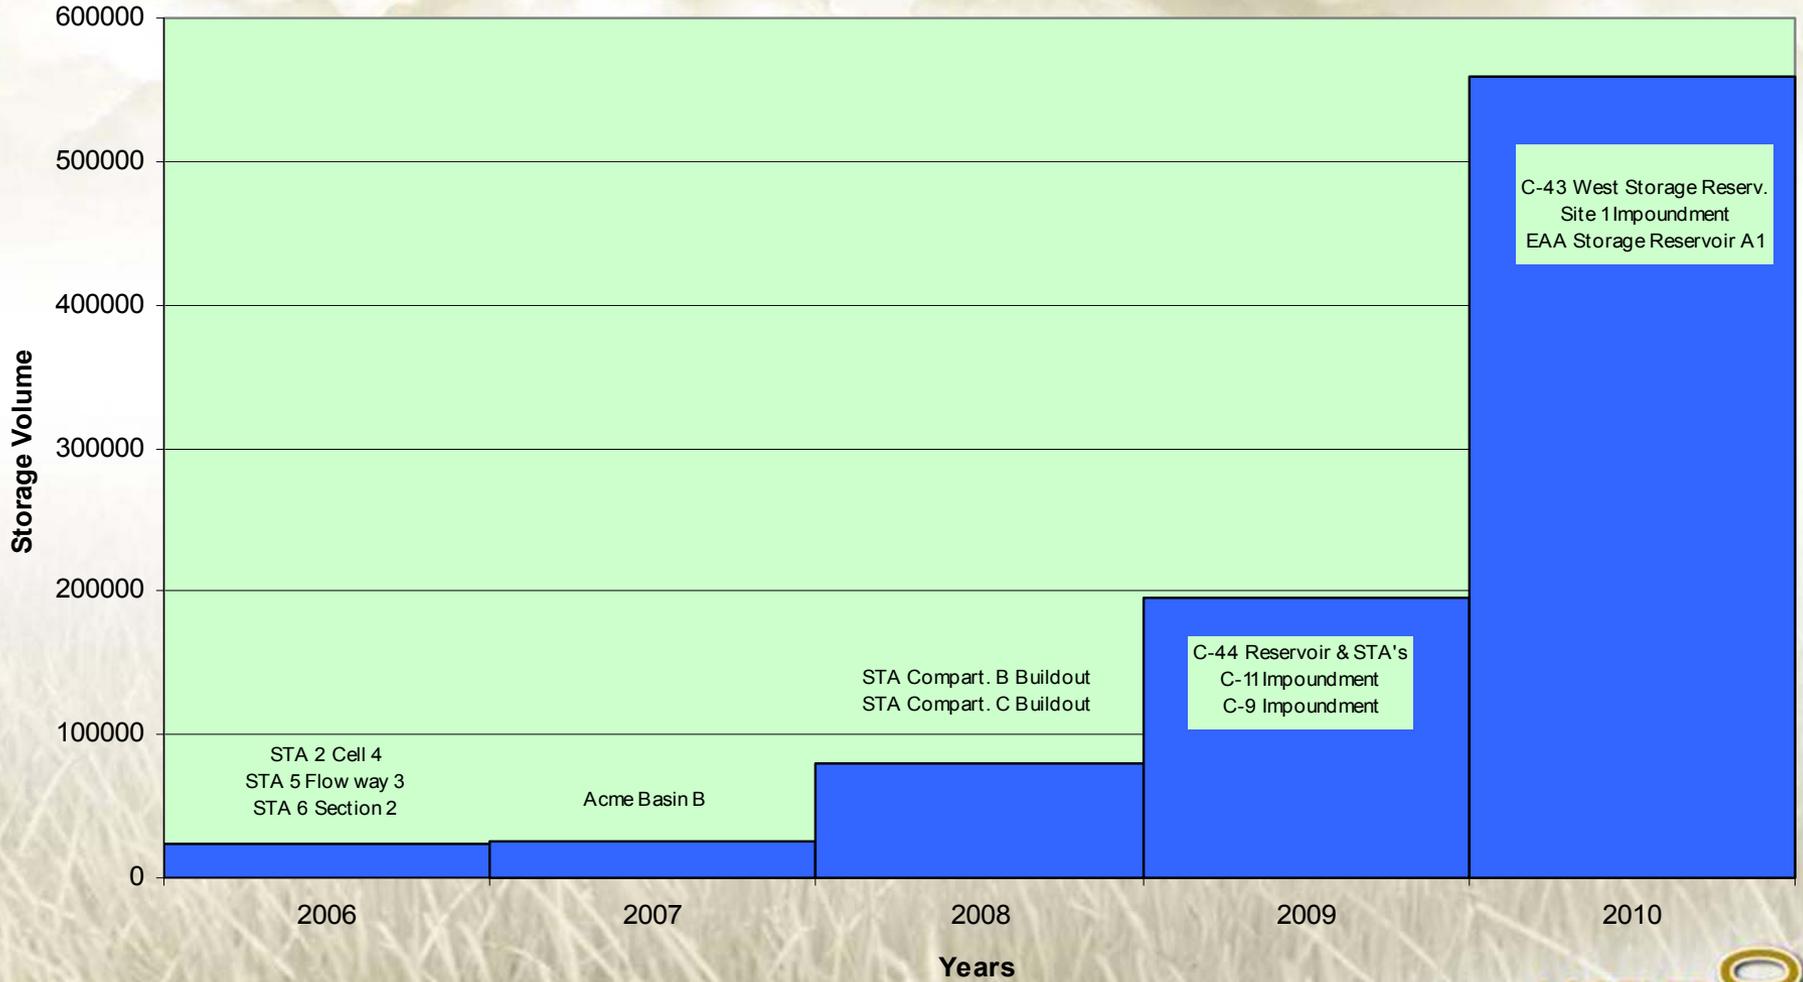

PIR STATUS FOR ACCELER8 PROJECTS

As of October 31, 2005

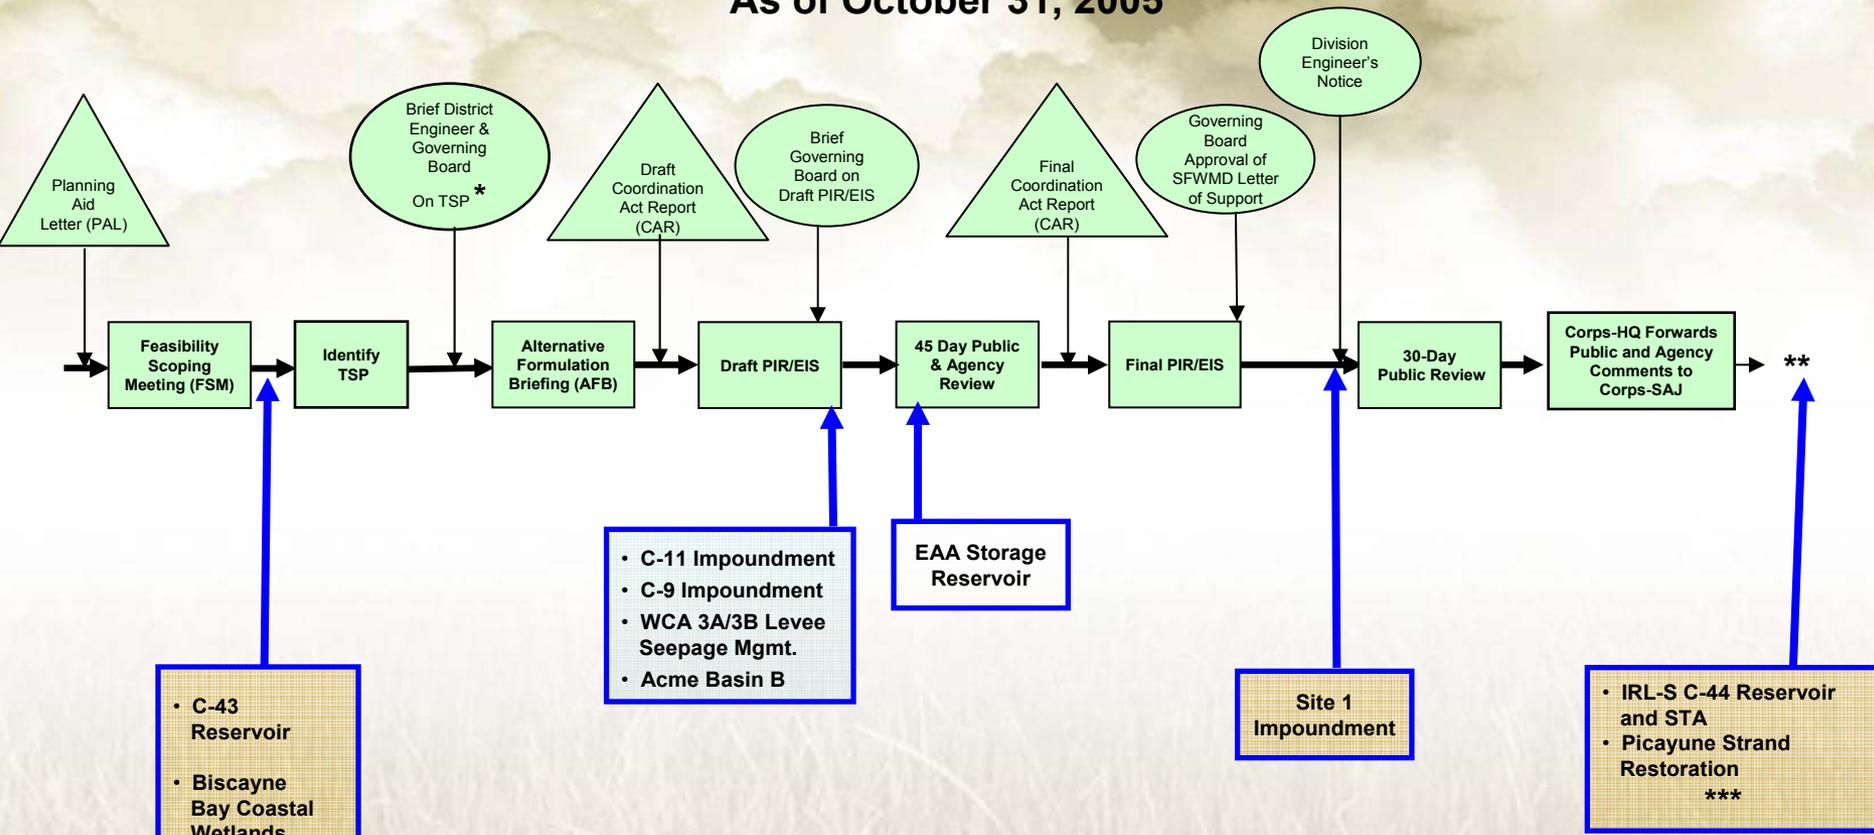

- C-43 Reservoir
- Biscayne Bay Coastal Wetlands
- C-111 Spreader Canal


- C-11 Impoundment
- C-9 Impoundment
- WCA 3A/3B Levee Seepage Mgmt.
- Acme Basin B

EAA Storage Reservoir

Site 1 Impoundment


- IRL-S C-44 Reservoir and STA
- Picayune Strand Restoration
- ***

* District Engineer approval of TSP is required prior to initiating intermediate design under Acceler8.
 ** PIR Process will continue beyond the "Prepare Responses to Public Comment", leading to a separate ROD for the PIR and a Chief's Report.
 *** Final Chief of Engineers Report Completed



DESIGN STATUS FOR ACCELER8 PROJECTS

As of October 31, 2005

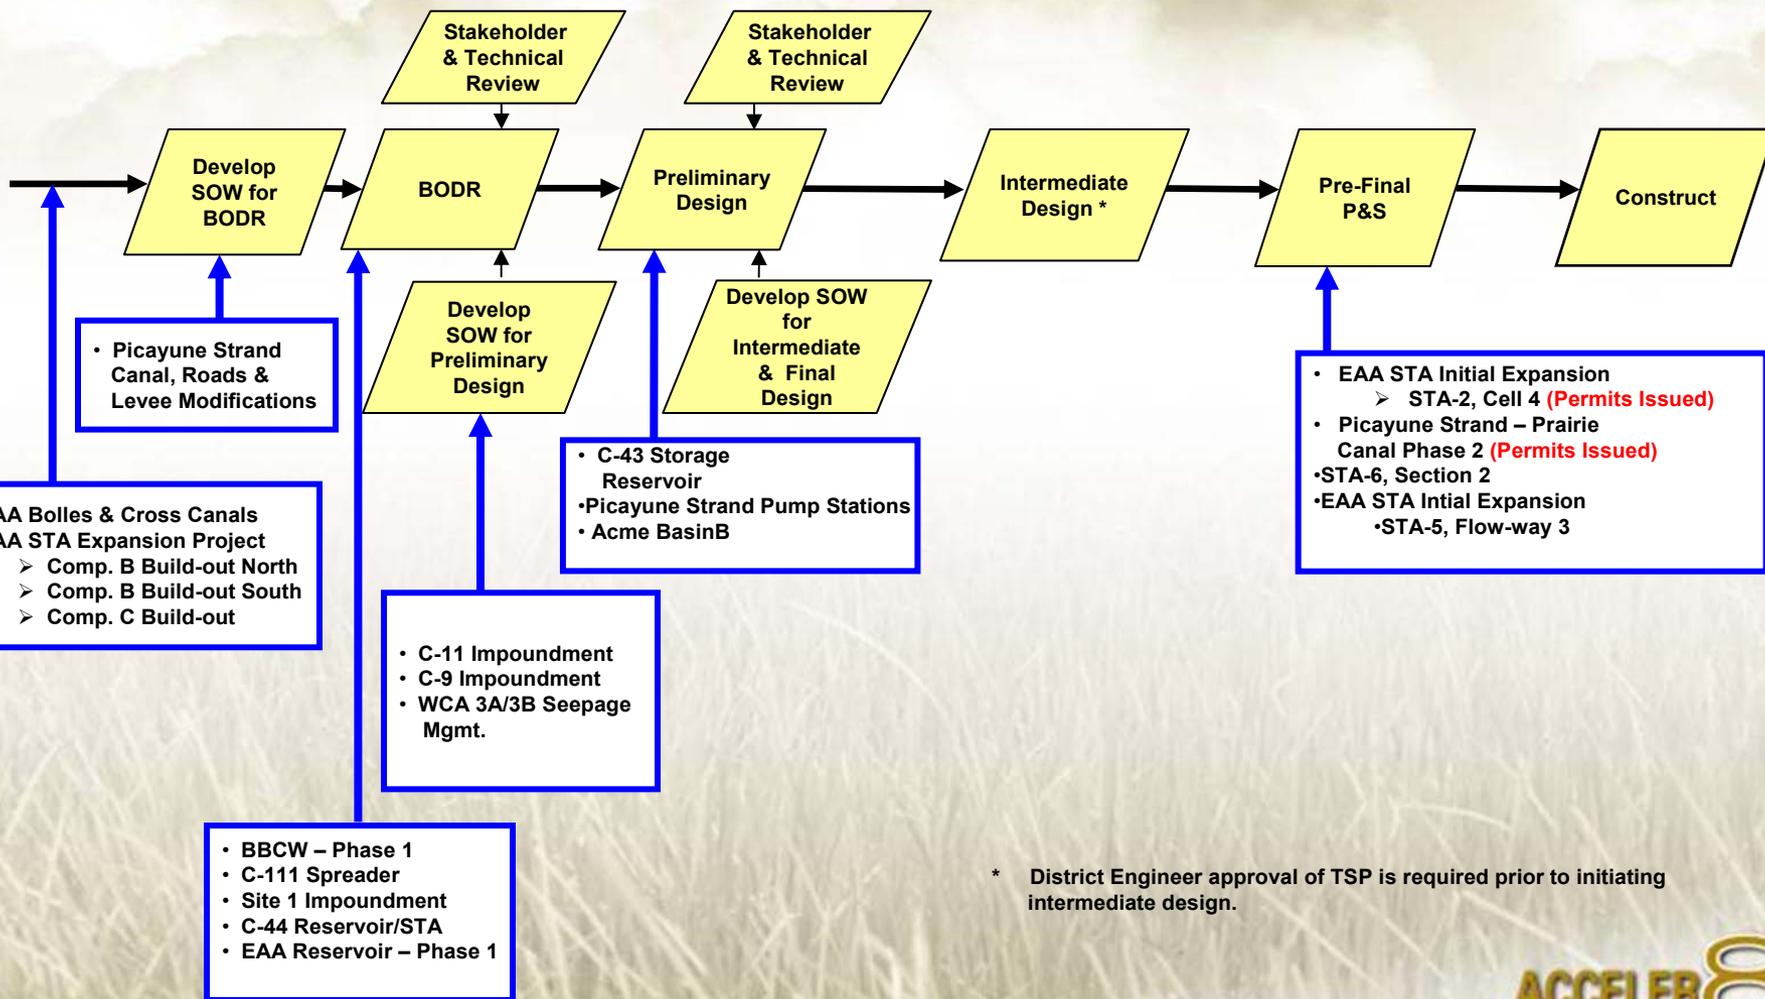

* District Engineer approval of TSP is required prior to initiating intermediate design.

Current Activities

- Pending Construction Solicitations
 - STA 2, Cell 4
 - STA 5, Flowway 3
 - STA 6, Section 2
 - C-43 Test Cells
 - C-44 Test Cells



Upcoming Activities

- Continued BODR Development
 - C-111 Spreader Canal
 - Biscayne Bay Coastal Wetlands
 - C-9 Impoundment
 - C-11 Impoundment
 - WCA-3A/3B Seepage Management
 - Picayune Strand Levee & Spreader Canal
 - C-44 Reservoir & STA



Solicitation Summary

Project	Package Available to Contractors	Governing Board
C-43 Test Cells	October 10, 2005	December 2005
STA 2 Cell 4	October 14, 2005	December 2005
STA 5 Flowway 3	October 21, 2005	December 2005
STA 6 Section 2	November 10, 2005	January 2006
CM @ Risk	November 10, 2005	January 2006
Contractor Prequal	November 15, 2005	N/A
C-44 Test Cells	November 15, 2005	February 2006
Picayune Demolition	November 23, 2005	January 2006

Acceler8 Anniversary Major Accomplishments

- Established Acceler8 Team
- Relocated Off-site
- Programmatic Inter-agency Coordination
- Implemented Project Control & Program Management Processes
- Initiated Design Criteria Development
- Implemented Document & QA/QC Controls
- Implemented Outreach Program



Acceler8 Anniversary Major Accomplishments

- Completed Basis Of Design Reports for several major projects
 - STA 6, Section 2
 - STA 5, Flowway 3
 - STA 2, Cell 4
 - C-43 Reservoir
 - Picayune Strand Pumping Stations
 - ACME Basin B
- Completed Engineering Design for...
 - STA 6, Section 2
 - STA 5, Flowway 3
 - STA 2, Cell 4
 - EAA Reservoir Test Cells
 - C-43 Reservoir Test Cells
- Completed EAA Test Cell Construction & Testing
- Held Major Construction Outreach Symposiums



QUESTIONS
